

Ice Machine Installation Checklist

Subject: CNF Model Countertop Model Ice Machines COUNTERTOP MODELS


⚠ Warning

Authorized Service Representatives are obligated to follow industry standard safety procedures, including, but not limited to, local/national regulations for disconnection / lock out / tag out procedures for all utilities including electric, gas, water and steam.

MANITOWOC RECOMMENDS A FACTORY AUTHORIZED SERVICE COMPANY OR DISTRIBUTOR AUTHORIZED SERVICE DEALER FOR INSTALLATION.

Section 2 (Installation) of the Installation, Operation and Maintenance manual must be followed to ensure proper installation steps are completed. Read the manual thoroughly before operating, installing or performing maintenance on the equipment.

Please refer to our website: <https://www.manitowocice.com/> for training videos, warranty registration, factory authorized service locator and additional service literature.

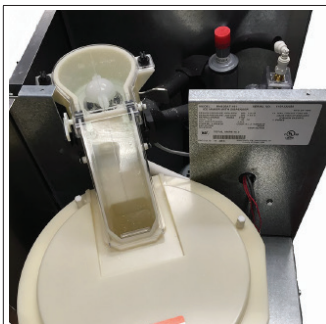


1. Confirm the Model and Serial number match the specification.
 - Model and serial tag can be found on the rear panel or inside next to the ice bin.



2. Has the ice machine been installed where ambient temperatures will remain in the range of 45° - 110°F?




3. Have minimum clearances around the ice machine been met as stated in the Installation, Operation and Maintenance manual?



4. Have all electrical and water connections been completed per the guidelines in the Installation, Operation and Maintenance manual and meet local, state and national code standards?




5. Is the electrical supply on a dedicated circuit?



6. Has the supply voltage been tested and confirmed against the rating on the model/serial tag?

Voltage

	7. Is the potable water supply on a dedicated 3/8" line? • Temperature range of 40° - 90°F • Supply pressure between 20 psi to 80 psi • Does the water filtration meet the ice machine production capacity? • AR-PRE - all • AR-10000 - all	 11. Has the owner/operator completed the warranty registration? SCAN THE QR CODE WITH YOUR SMART DEVICE TO COMPLETE YOUR WARRANTY REGISTRATION.
	8. Is the drain line correctly installed and contains a union? • Drain lines must have 1.5-inch drop per 5 foot, with no traps • Drain lines must meet drain termination air gap local code requirements	
	9. Is the ice machine level?	
	10. Has the ice machine and storage bin been sanitized prior to use?	
